ID	Task Name	Duration	Start	Finish	Predecessors
1	**Stage 0 - Strategic Definition**	**7 days**	**Fri 05/01/18**	**Mon 15/01/18**	
2	Procurement: standstill period	7 days	Fri 05/01/18	Mon 15/01/18	
3	Procurement: contract award	0 days	Mon 15/01/18	Mon 15/01/18	2
4	**Stage 1 - Preparation and Brief**	**10 days**	**Mon 15/01/18**	**Fri 26/01/18**	
5	Site Information (measured survey)	2 wks	Mon 15/01/18	Fri 26/01/18	
6	**Stage 2 - Concept Design**	**65 days?**	**Mon 29/01/18**	**Fri 27/04/18**	**4**
7	Concept Design	4.8 wks	Mon 29/01/18	Thu 01/03/18	
8	Cost Information	5 days	Mon 05/03/18	Fri 09/03/18	7
9	Programme (draft paper and review)	7 days	Mon 12/03/18	Tue 20/03/18	8
10	Programme (Cabinet meeting)	0 days	Wed 21/03/18	Wed 21/03/18	9
11	Concept Design (existing)	12 days?	Mon 05/03/18	Tue 20/03/18	
12	Concept Design (proposed)	18 days	Wed 21/03/18	Fri 13/04/18	10,11
13	Project Strategies	5 days	Mon 16/04/18	Fri 20/04/18	12
14	Final Project Brief	5 days	Mon 23/04/18	Fri 27/04/18	13
15	Information Exchange	0 days	Fri 27/04/18	Fri 27/04/18	14
16	**Stage 3 - Developd Design**	**35 days**	**Mon 30/04/18**	**Fri 15/06/18**	**6**
17	Developed Design	5 wks	Mon 30/04/18	Fri 01/06/18	
18	Cost Information	2 wks	Mon 04/06/18	Fri 15/06/18	17
19	**Stage 4 - Technical Design**	**115 days**	**Mon 18/06/18**	**Fri 23/11/18**	**16**
20	Technical Design (GAs)	2 wks	Mon 18/06/18	Fri 29/06/18	
21	Technical Design (building fabric)	6 wks	Mon 25/06/18	Fri 03/08/18	20SS+1 wk
22	Procurement (building fabric)	6 wks	Mon 06/08/18	Fri 14/09/18	21
23	Technical Design (fitout)	12 wks	Mon 23/07/18	Fri 12/10/18	21FS-2 wks
24	Procurement (fitout)	6 wks	Mon 15/10/18	Fri 23/11/18	23
25	Technical Design (mechanical)	8 wks	Mon 18/06/18	Fri 10/08/18	
26	Technical Design (electrical)	8 wks	Mon 18/06/18	Fri 10/08/18	
27	Procurement (mech and elec)	6 wks	Mon 13/08/18	Fri 21/09/18	26
28	Technical Design (lift)	2 wks	Mon 13/08/18	Fri 24/08/18	26
29	Procurement (lift)	6 wks	Mon 27/08/18	Fri 05/10/18	28
30	Technical Design (drainage)	2 wks	Mon 13/08/18	Fri 24/08/18	26
31	Procurement (drainage)	4 wks	Mon 27/08/18	Fri 21/09/18	30
32	**Stage 5 - Construction**	**145 days**	**Mon 27/08/18**	**Fri 15/03/19**	
33	Construction (building fabric)	16 wks	Mon 17/09/18	Fri 04/01/19	22
34	Construction (fitout)	16 wks	Mon 26/11/18	Fri 15/03/19	24
35	Construction (mech and elec)	24 wks	Mon 24/09/18	Fri 08/03/19	27
36	Construction (lift)	22 wks	Mon 27/08/18	Fri 25/01/19	28
37	Construction (drainage)	4 wks	Mon 24/09/18	Fri 19/10/18	31
38	**Stage 6 - Handover and Close Out**	**10 days**	**Mon 18/03/19**	**Fri 29/03/19**	**32**
39	Handover of building	2 wks	Mon 18/03/19	Fri 29/03/19	

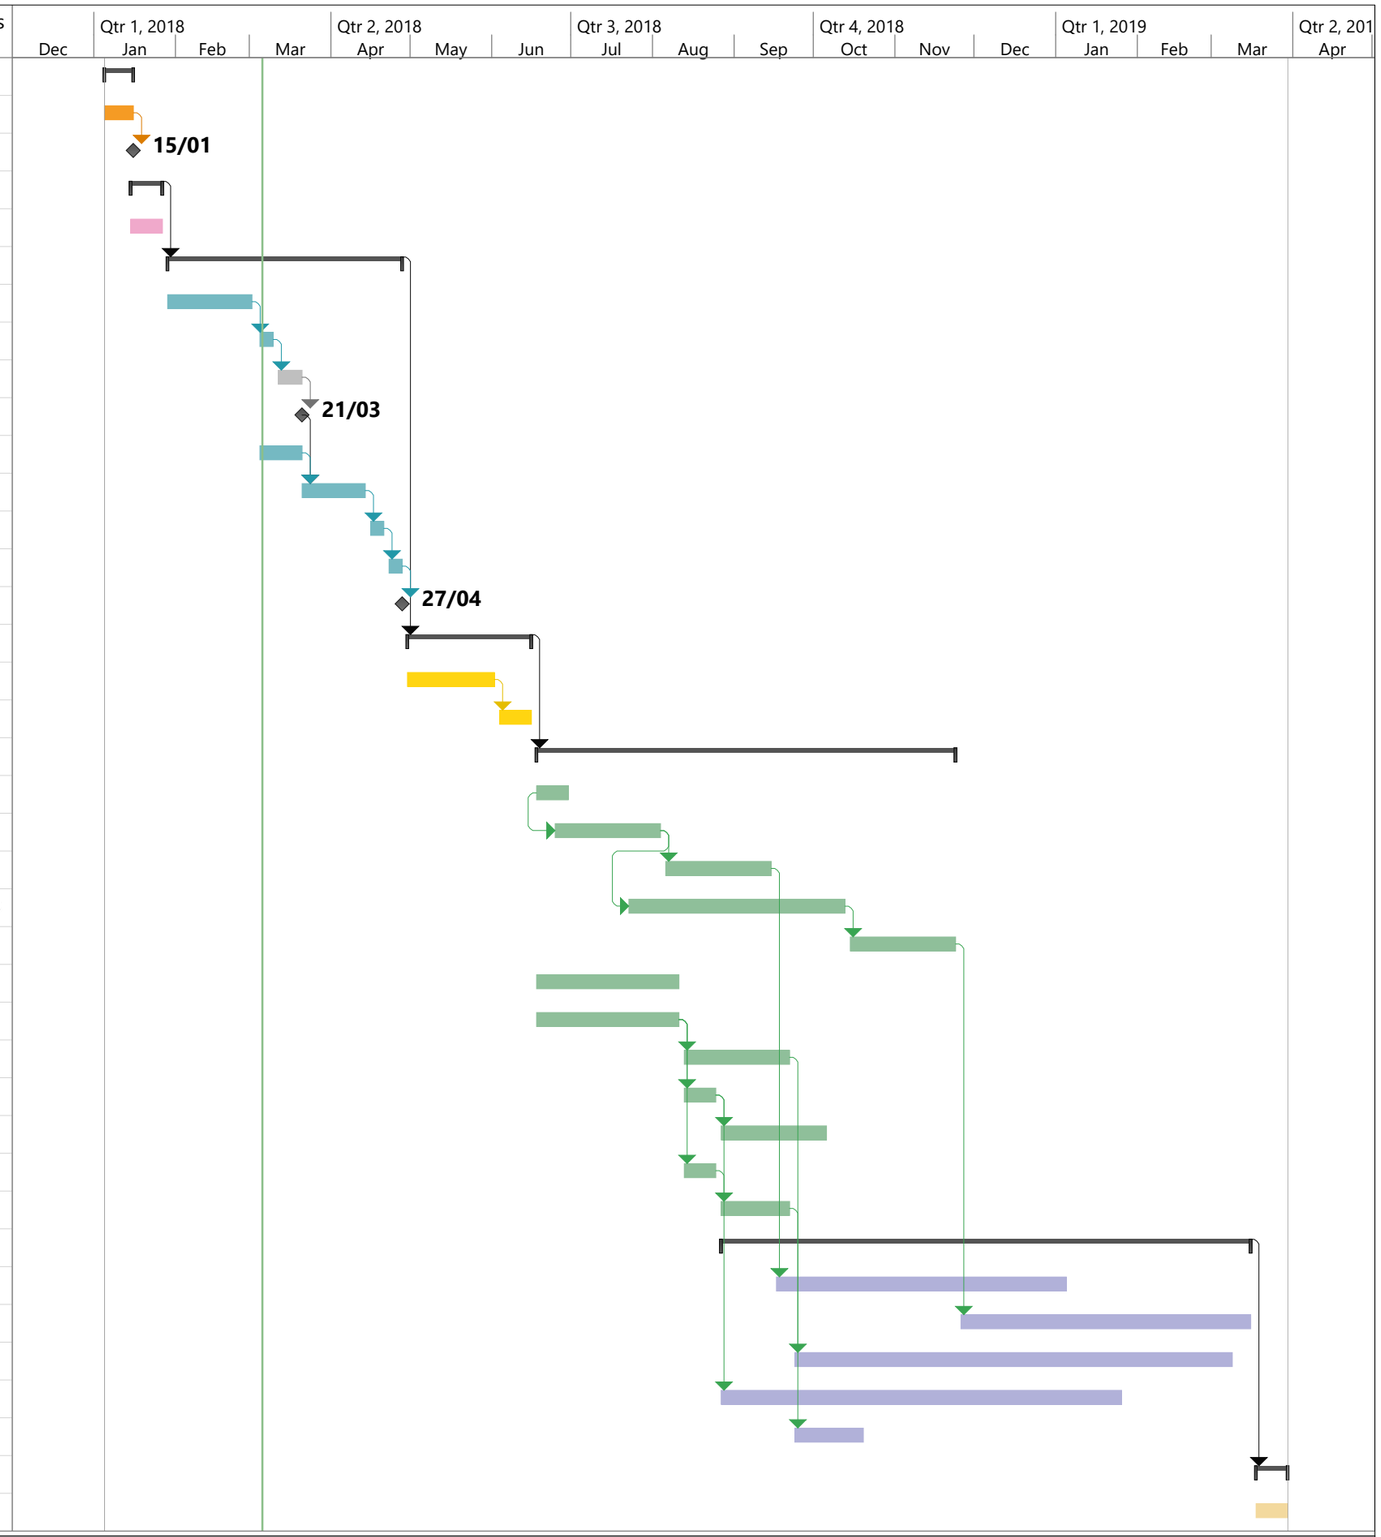

Project: LAR-S2-ProjectProgramme
Date: Tue 06/03/18

Task | Split | Milestone | Summary | External Tasks
